

**OHM Remediation
Services Corp.**

A Subsidiary of OHM Corporation

September 18, 1996

Ms. Kate Landman
Atlantic Division Code 18232
Naval Facilities Engineering Command
1510 Gilbert Street
Norfolk, VA 23511-2699

Re: Contractor's Closeout Report
Site 41, MCAS New River
Contract N62470-93-D-3032; Delivery Order 0101
MCB Camp Lejeune, NC

Dear Ms. Landman:

Submitted for your review and approval is this letter Closeout Report for D.O. 0101, Site 41, MCAS New River, MCB Camp Lejeune, N.C.

Overview

OHM installed fencing and signs in support of D.O. 0101 to restrict access to Site 41 at the Marine Corps Air Station. Site access was required to be restricted because Site 41 was previously used as an open burn dump from 1946 to 1970. In addition to construction debris and several other types of waste, it is reported that in the mid-1960s, at least two waste disposal incidents occurred involving the disposal of drummed wastes from trucks. These wastes were described as being similar to the types of wastes disposed of at Site 69 (Rifle Range Chemical Dump).

Field Activities

OHM commenced field activities on August 8, 1996 and completed the field work on August 15, 1996. A photo log is attached documenting the work performed.

OHM installed 150 feet of fencing with twin 10 feet wide swing gates across a dirt road at the southeast access to the site. At the west access via the same road OHM installed 50 feet of fence with a 16 feet swing gate. Figure 1 identifies the as built locations of the fencing and gates.

Thirty four 24 inches by 24 inches metallic signs were installed around the east, west and southern boundaries of the site. These signs were posted on existing trees and adjacent to the two gates. The signs have a yellow background with red lettering. Figure 1 also indicates the locations of the signs.

Health & Safety Issues

The project was completed safely without any accidents or near misses.

Schedule Impacts/Changes


The project was delayed awaiting final approval from the New River Air Station of the sign wording and locations. The signs were changed from a green background with white lettering to a yellow background with red lettering. The final wording on the signs is as follows:

**KEEP OUT
HAZARDOUS
WASTE
SITE**

Additional signs were installed to encompass the southern boundary of the site (34 versus 15).

The final inspection and approval of the site was conducted with the ROICC on September 18, 1996.

Very truly yours,
OHM Remediation Services, Inc.



James A. Dunn, Jr., P.E.
Senior Project Manager

Attachments



- I. Photo Log
- II. Figure 1

pc: See Page 3

Page 3

Closeout Report, Site 41

pc: Neal Paul - IRD/EMD w/enclosures (2)
Lt. Hansen - ROICC w/enclosures
Matt Bartman - Baker Environmental w/enclosures
Dave Lown - NCDEHNR w/enclosures
John Franz - OHM w/enclosures
Jerry Haste - NAVFACENGCOM w/enclosures
Gena Townsend - EPA Region IV w/enclosures
OHM Project File/18421 w/enclosures
Dwayne Currie - OHM w/enclosures
Greg Gilles - OHM w/enclosures
Chuck Lawrence - Stone & Webster w/enclosures
Project File 18421-14.3 w/enclosures

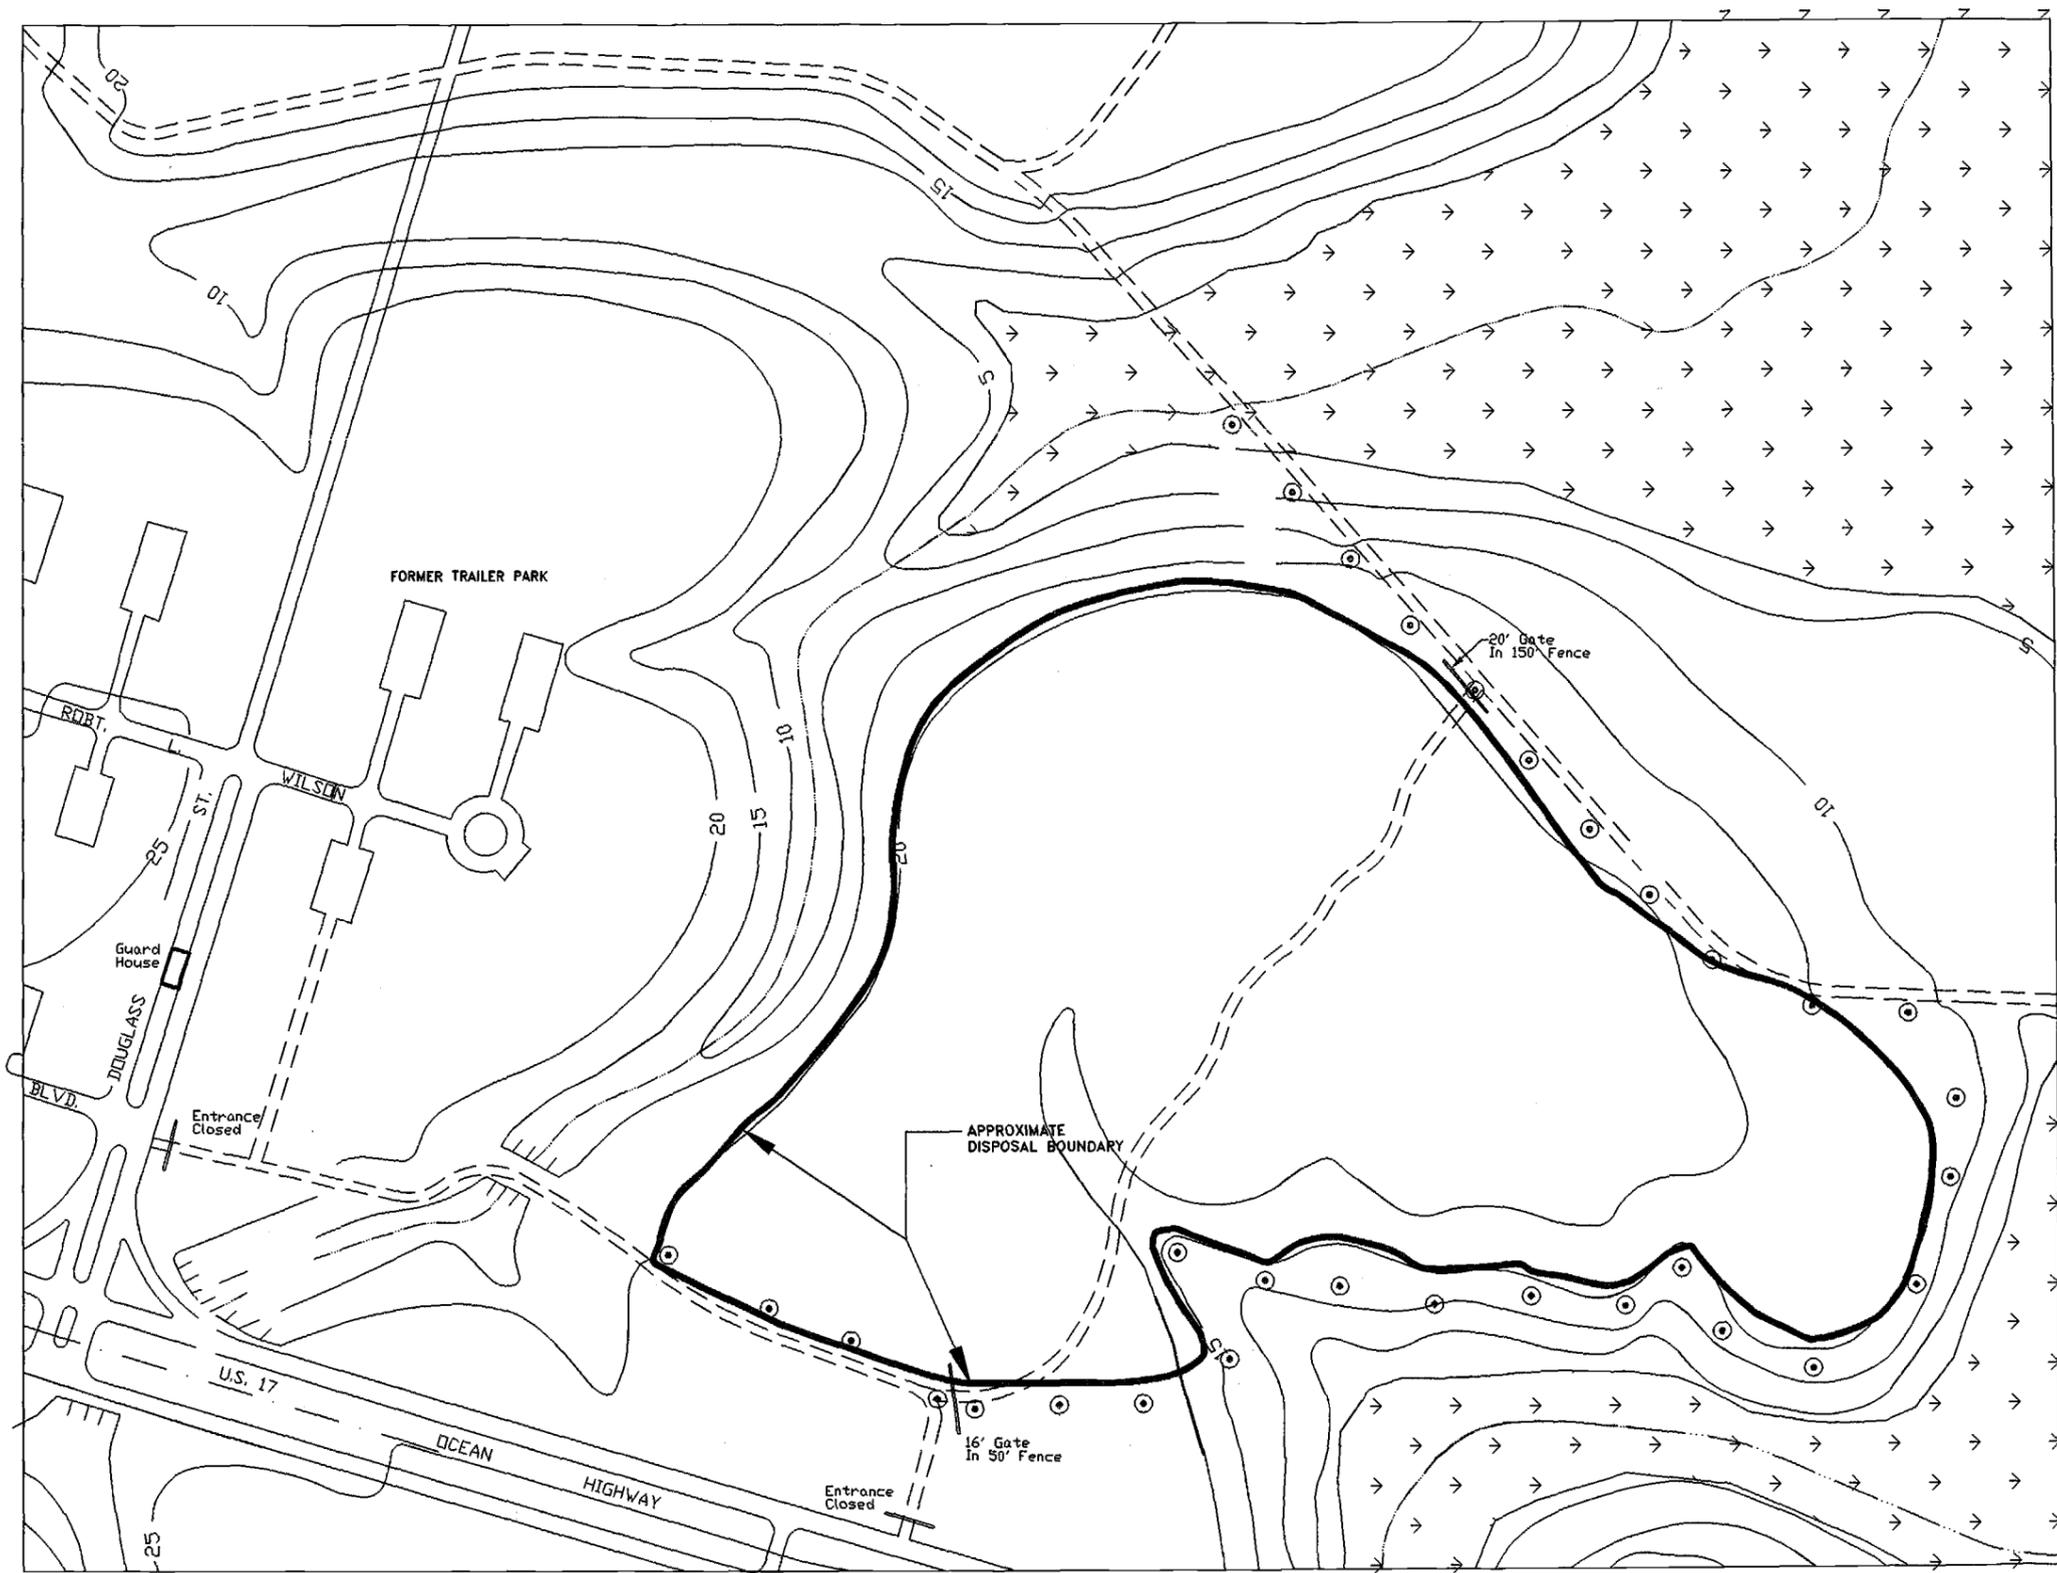

LEGEND

- MARSH
- TOPOGRAPHIC ELEVATION LINES (FEET, MEAN SEA LEVEL)
- ROAD (IMPROVED)
- ROAD (UNIMPROVED)
- INTERMITTENT STREAM
- SIGN @ 200' O.C. INSTALLED ON GATES OR EXISTING TREES

SOURCE: LANTDIV, OCT. 1991, BAKER 1996

OHM Remediation Services Corp. NORCROSS, GEORGIA A SUBSIDIARY OF OHM CORPORATION		
DRAWN BY	J. LANGE	3/15/96
CHECKED BY	J. DUNN	3/15/96
APPROVED BY	-	DATE
REV. 0	SHEET # -	PROJECT NO. 18421

FIGURE 2
AS BUILT
GENERAL ARRANGEMENT MAP
SITE 4I-CAMP GEIGER DUMP
 D.O. 101
 MCB CAMP LELEUNE
 PREPARED FOR
 LANTDIV

01808 II 012

D:\OHM\LANTDIV\LELEUNE\18421\FIG2.DWG



Project No. 18421 **Date: 8/14/96**
Contract No. N62470-93-D-3032
Delivery Order: 101
Description: 150-foot section of fence with 20-foot gate on the east end of the spine road



Project No. 18421 **Date: 8/14/96**
Contract No. N62470-93-D-3032
Delivery Order: 101
Description: 50 foot section of fence with 20 foot gate on the west end of the spine road

01808 IIBIV



Project No. 18421 **Date: 8/14/96**
Contract No. N62470-93-D-3032
Delivery Order: 101
Description: Warning sign posted at 200 foot intervals
around the southern end



Project No. 18421 **Date: 8/14/96**
Contract No. N62470-93-D-3032
Delivery Order: 101
Description: Warning sign posted on the gate of the west
end of the spine road



Project No. 18421

Date: 8/14/96

Contract No. N62470-93-D-3032

Delivery Order: 101

**Description: Warning sign posted on the gate of the east
end of the spine road**
